

Apartment Refurbishment Timeline & Payment Schedule

Property: Al Mass Tower, Apartment 2002, Dubai

Project Start: To Be Discussed


Planned Duration: 6 Weeks (5 Weeks Works + 1 Week Snagging Only)



Apartment Refurbishment Journey (6 Weeks)



Integrated Payment Process & Timeline

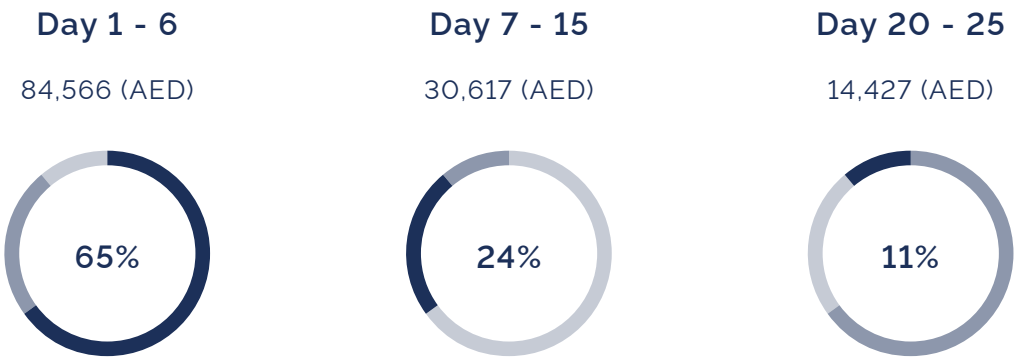

Payment Process

Project Stage	Amount (AED)	Percentage
Day 1	18,705.45	14.43 %
Day 6	65,860.06	50.81 %
Day 7	12,623.45	9.73 %
Day 15	17,993.30	13.88 %
Day 20	9,016.75	6.96 %
Day 25	5,410.05	4.17 %
TOTAL	129,609.06	100%

Project Cost Summary

Term	Cost (AED)
Bathroom Works	36,067
Main Refurbishment	27,682
Kitchen	50,217
Materials	15,643
TOTAL	129,609



Project Phases & What Happens

Phase	Timeline	What's Happening	Responsible Party
Phase 1 Project Start Mobilization	Day 1	Site mobilization, project setup, bathroom preparation	Blue Squad / KIVI
Phase 2 Demolition & Preparation	Days 1 – 5	Demolition, strip-out, waste removal, site clearance	All Contractors
Phase 3 Material Release & Ordering	Days 6	Kitchen production released, bathroom tiles & sanitary ware ordered	IKEA / Rak Ceramics
Phase 4 Post-Demolition Progress	Days 7	Completion of demolition and waste removal milestone	KIVI
Phase 5 Main Refurbishment Works	Days 6 – 15	MEP works, carpentry, painting, coordination	Blue Squad
Phase 6 Bathroom Waterproofing & Tiling	Days 11 – 20	Bathroom waterproofing, tiling, and fit-out works	KIVI
Phase 7 Kitchen Installation & Quartz Works	Days 21 – 26	Kitchen cabinet installation, quartz measurement and fitting	IKEA
Phase 8 Bathroom Handover	Day 25	Completion of bathroom works and formal handover	KIVI
Phase 9 Snagging & Final Adjustments	Days 31 – 35	Snagging, rectifications, testing, final quality sign-off	All Contractors
Final Phase Project Completion	Day 35	Final completion and project close	All Parties

Advance & Early Payment Summary (Day-Based)

Party	Timing	Amount (AED)
Blue Squad	Day 1	9,688.70
KIVI	Day 1	9,016.75
IKEA	Day 6	50,216.81
Rak Ceramics	Day 6	15,643.25
TOTAL	By Day 6	84,565.51
